

Fox Cities Exhibition Center

Weekly Update - 12/04/2017

Key Progress Points

- ◇ **Radisson Paper Valley Hotel Work:** MEP work continues, and interior stud framing and drywall has started. Elevator and escalator finishes are ongoing. Roof work is complete. The work platform has been removed and the ceiling grid on the second level has been installed.

- ◇ **Concrete:** The patio in Jones Park has been poured. Site concrete nears completion.

- ◇ **Exterior Work:** Omni has installed the pre-function curtain wall and glazing leading into Jones Park. Corcoran continues installing metal wall panel. Landscaping is complete along Eighth Street and in the staircase planters. Landscaping continues in front of the plaza deck. Loading dock equipment is being installed, as well as overhead doors in the exhibition space. The large overhead door at the top of the ramp has been installed. Demolition of the warming shelter in Jones Park is complete.

- ◇ **Finishes:** Spies Painting continues to paint in all areas. Acoustical wall panels were installed in the exhibition space. Tile has been installed in the pre-function bathroom. VerHalen is finishing soffits, the ceiling grid, and framing/drywall/finishing at the Radisson. Doors and hardware are being installed, along with bathroom partitions and fixtures. Elevator and escalator finishes continue.

- ◇ **Conditions & Safety:** Site conditions are good; there were no injuries this week.

Progress Photographs




Fox Cities Exhibition Center signage has been installed on the crosswalk.



The exhibition hall has been painted and the acoustical wall panels were installed.



Glass handrail and other finishes are being installed on the escalators.

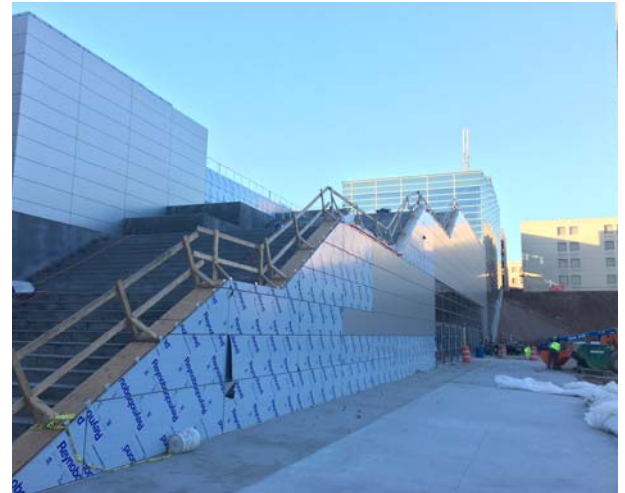

The plaza stairs and Jones Park patio have been poured. Handrail installation has begun on the plaza level, and installation on the stairs will begin soon.
