

# Fox Cities Exhibition Center

## Weekly Update - 02/27/2017

---

### Key Progress Points

- ◇ **Excavation:** *Excavation of the Tier 2 soils was nearly completed this week, with only a small portion to be taken out at the beginning of next week. This area had to remain in place due to Michels conducting several re-grouts of their tieback anchors. In the coming week, excavation of the Tier 3 soils will begin bringing the elevation down to the building floor elevation.*
  
- ◇ **Tieback Anchors:** *Work on Tier 2 tieback anchors progressed on the north and south end of the project site with only a few days worth of work left along Elm Street. Once these are completed, the crews will begin to follow Calnin & Goss at the Tier 3 level. At these elevations, the crews will be able to make good time due to no obstructions from the abandoned building structures as experienced in the upper tiers.*
  
- ◇ **Conditions & Safety:** *The site was well-maintained and weather remained favorable until Thursday evening, which brought snowy conditions. The crews spent the majority of Friday ensuring the site and surrounding areas were cleared of snow and ice. Preventive maintenance was also conducted in preparation for the coming week. No injuries occurred this week.*

## Progress Photographs




Progress of the tieback anchors along Eighth Street.



View of the northeast corner of the building footprint. Work will begin in the coming week on the Tier 3 excavation in this area.



Closer look at the type of tieback anchor being used. Unlike the top tier, the bottom tiers utilize a stranded cable in lieu of a threaded rod.

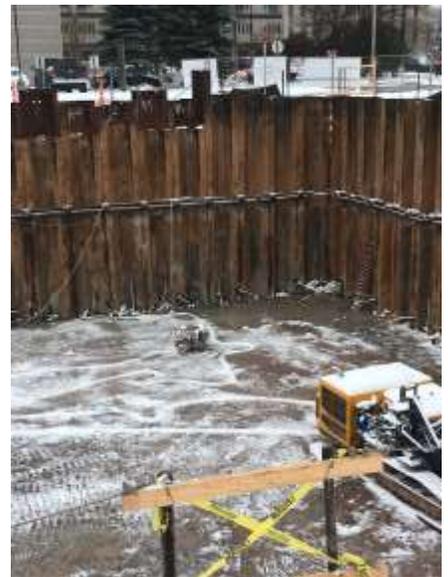

Tiebacks have been installed to the corner of Eighth and Elm Street. Walers will be installed in the coming week.
