

Fox Cities Exhibition Center

Weekly Update - 03/06/2017

Key Progress Points

- ◇ **Excavation:** *Excavation of Tier 3 began this week, with the northeast corner being completed. Calnin & Goss continued to work hand-in-hand with Michels at the perimeters to remove soils and allow Michels to auger the tieback anchor holes. Extra work had to be done in certain areas to remove the old school footings that were left in the soils. Mass excavation of the Tier 3 soils will begin in the upcoming week and should proceed faster than the other tiers due to this lift only being approximately six feet.*

- ◇ **Tieback Anchors:** *The remaining Tier 2 tiebacks and re-grouts of the Tier 2 tieback anchors were completed, and work on Tier 3 tieback anchors began later in the week. Footings from the old school continued to be a problem for the crews, however, using a duplex auger they were able to core through the concrete footings with limited schedule impact. Work will continue in the coming week on the Tier 3 tieback anchors, as well as the final testing of the tieback anchors along Elm Street.*

- ◇ **Conditions & Safety:** *Throughout the week the temperatures remained fairly low, keeping the site limited in mud. During the middle of the week a rather large snowstorm hit, which caused Calnin & Goss to work on snow removal in the site and surrounding areas. Despite this, there was no impact to the schedule this week due to the weather. No injuries occurred this week.*


Progress Photographs




Some of the old school foundations that Calnin & Goss worked on removing this past week.



Delivery of the pipe piles that will be placed below the building footings. This work is anticipated to start mid-March.

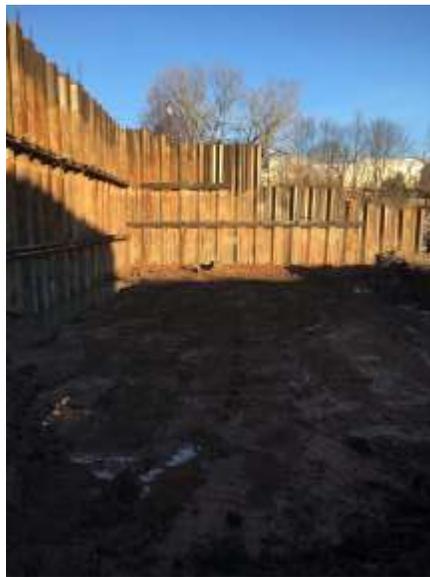

Progress of the Tier 3 excavation in the northeast corner.

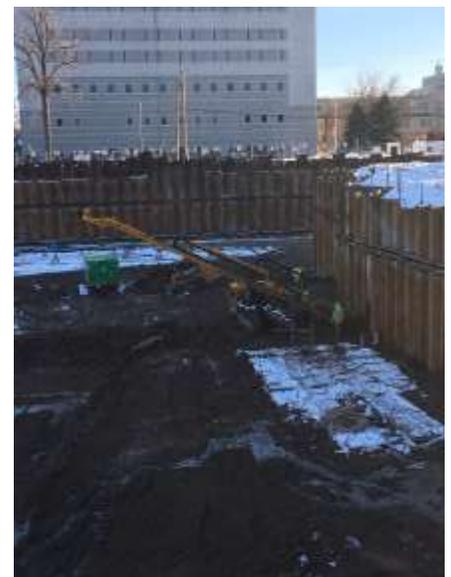

Michels crew working on auguring through the old school foundations along Elm Street.
