



Fox Cities Exhibition Center

Weekly Update - 04/03/2017

Key Progress Points


- ◇ **Excavation:** *Excavation of the various pile caps continued throughout the week. Calnin & Goss worked hand-in-hand with Miron's concrete crew and Michels Foundations to determine which pile caps needed to be dug out. Wet conditions also created continuous work for Calnin & Goss to ensure that the site was maintained enough to allow the various equipment to freely maneuver.*

- ◇ **Tieback Anchors/Pipe Piles:** *Final grouting of the tiebacks occurred and the testing is nearly complete for all of the tieback anchors. Once finished early next week, the crew handling the testing will be able to move on to assist the pipe piling crews conduct installations. Throughout the week, the pipe piling crew worked vigorously to ensure they stayed ahead of the concrete and rebar crews and were able to install more than the forecasted amounts.*

- ◇ **Concrete:** *Rebar crews began work on tying what they could for rebar already onsite. The freight elevator pit as well as the northeast elevator pits were completely tied in preparation for the concrete crews to pour in the upcoming week. Some of the pile caps in the northeast corner were completely installed as well.*

- ◇ **Conditions & Safety:** *Extremely muddy conditions threatened to hinder the job, however, between the various trades coordinating together, no work was delayed. Extra efforts were implemented to ensure enough traction pads were laid down and large crane mats, constructed of thick timber planks, were placed to allow the crews to maneuver and work easily. No injuries occurred this week.*


Progress Photographs

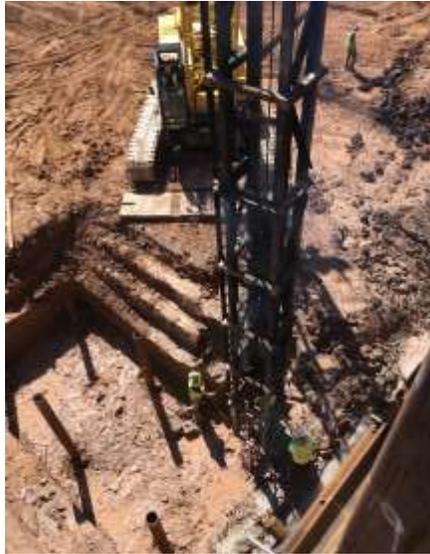


Michels crew installing the pipe piling along Lawrence Street.



The rebar cage for the freight elevator pit. The pipe in the middle is the hydraulic shaft for the elevator itself.

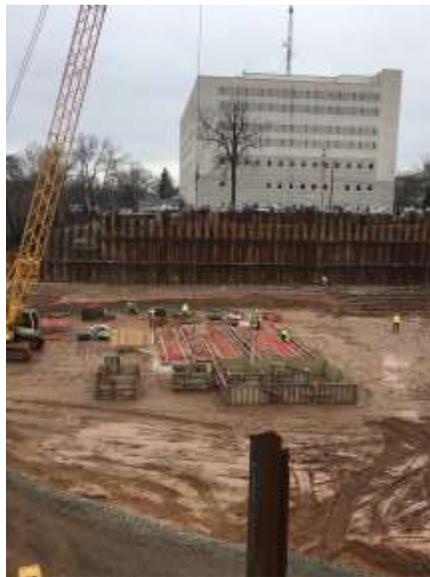

Miron's concrete crews working on piecing together the interior form for the freight elevator's walls. Once erected, this will be swung into place by the crane when ready to pour.

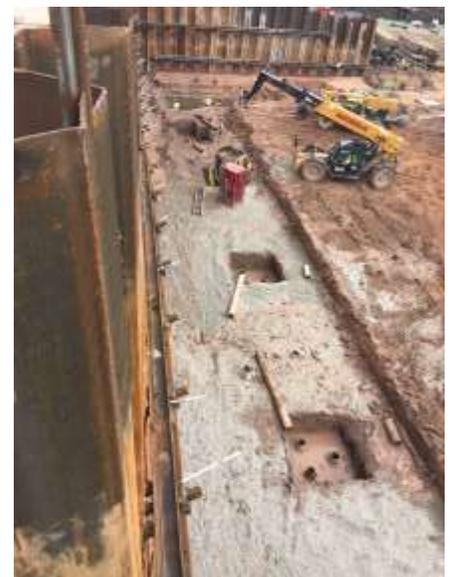

Michels working on filling the pipe piling along Lawrence Street with concrete.
